Appendix D
Construction Schedule

CONSTRUCTION

SITE WORK FOR BUILDING PAD

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish	Predecessors
220	OWNER NTP CONSTRUCTION	1	1	03JAN14	03JAN14	190*
1053	B SECTION - SET UP HONEYWELL FIELD OFFICE	30	30	06JAN14	17FEB14	1015*
1015	A SECTION - LINER REMEDIATION	80	80	06JAN14	28APR14	220*
1050	B SECTION - LINER REMEDIATION	65	65	21JAN14	21APR14	1015*
1315	D SECTION - PREPARE LINER FOR SHEET PILING	45	45	04FEB14	07APR14	1010*
1010	A SECTION - PILING	50	50	04FEB14	14APR14	1015*
1300	D SECTION - DOCK ST SHEET PILES AT SLURRY WALL	15	15	11FEB14	03MAR14	1010*
1058	B SECTION - HONEYWELL BUILDING DEMO	10	10	18FEB14	03MAR14	1053*
1055	B SECTION - PILING	35	35	18FEB14	07APR14	1010*
1305	D SECTION - WILL ST SHEET PILES AT SLURRY WALL	15	15	04MAR14	24MAR14	1300*
1060	B SECTION - PILE CAPS AND GRADING	50	50	04MAR14	12MAY14	1050*, 1055*, 1055*
1080	C SECTION - LINER REMEDIATION	45	45	18MAR14	19MAY14	1015*, 1015*
1020	A SECTION - PILE CAPS AND GRADING	60	60	18MAR14	10JUN14	1010*, 1010*
1310	D SECTION - DOCK ST OUTBOARD SHEET PILES	15	15	25MAR14	14APR14	1305*
1085	C SECTION - PILING	35	35	25MAR14	12MAY14	1055*
1070	B SECTION SLAB ON GRADE (SOG)	45	45	25MAR14	27MAY14	1060*, 1060*
1030	UNDER SLAB UTILITIES @ BLDG SOG	79	79	01APR14	22JUL14	1020*, 1020
1320	D SECTION - PILES FOR BRIDGE SLAB	15	15	15APR14	05MAY14	1310*, 1315*
1090	C SECTION - PILE CAPS AND GRADING	55	55	22APR14	09JUL14	1080*, 1085*, 1085*
1040	A SECTION SLAB ON GRADE (SOG)	40	40	29APR14	24JUN14	1020*, 1020*
1325	D SECTION - FORM & POUR DOCK ST BRIDGE SLAB	30	30	06MAY14	17JUN14	1320*
1095	C SECTION SLAB ON GRADE (SOG)	55	55	06MAY14	23JUL14	1090*, 1090*
1330	D SECTION - DOCK STREET LINER REMEDIATION	25	25	20MAY14	24JUN14	1325*, 1325*
1075	MILESTONE - B SECTION - COMPLETE SOG	0	0		27MAY14	1070*
1335	D SECTION - 6" PROTECTIVE SLAB	25	25	28MAY14	01JUL14	1330*, 1330*
1045	MILESTONE - A SECTION - COMPLETE SOG	0	0		24JUN14	1040*
1350	D SECTION - FINISH MILESTINE	0	0		01JUL14	1335*
1105	MILESTONE - C SECTION - COMPLETE SOG	0	0		23JUL14	1095*
1150	C1 SECTION - STRUCTURAL DECK	50	50	30OCT14	15JAN15	13125*
1165	C1 SECTION - UNDERGROUNG POWER CONDUIT	60	60	22DEC14	23MAR15	1150*
1170	C1 SECTION - UNDER GROUND SEWER	20	20	16JAN15	13FEB15	1150*
1155	C1 SECTION - POUR PLAZA WALLS	30	30	16JAN15	02MAR15	1150*
1160	C1 SECTION - ROADWAY STRUCTURAL FILL	15	15	03MAR15	23MAR15	1155*
1175	C1 SECTION - UNDER GROUND STORM WATER SYSTEM	40	40	24MAR15	18MAY15	1160*, 1165*, 1170
1180	C1 SECTION - UNDER GROUND WATER	20	20	07APR15	04MAY15	1175*
1185	C1 SECTION - 8" CONCRETE SLAB	10	10	19MAY15	02JUN15	1175*, 1180
1190	C1 SECTION - PAVERS	60	60	03JUN15	26AUG15	1185*
1195	C1 SECTION - ASPHALT PAVING	5	5	13AUG15	19AUG15	1190*
1200	C1 SECTION - LANDSCAPING	20	20	13AUG15	10SEP15	1190*
1250	C1 SECTION - FINISH MILESTONE	0	0		10SEP15	1195, 1200*

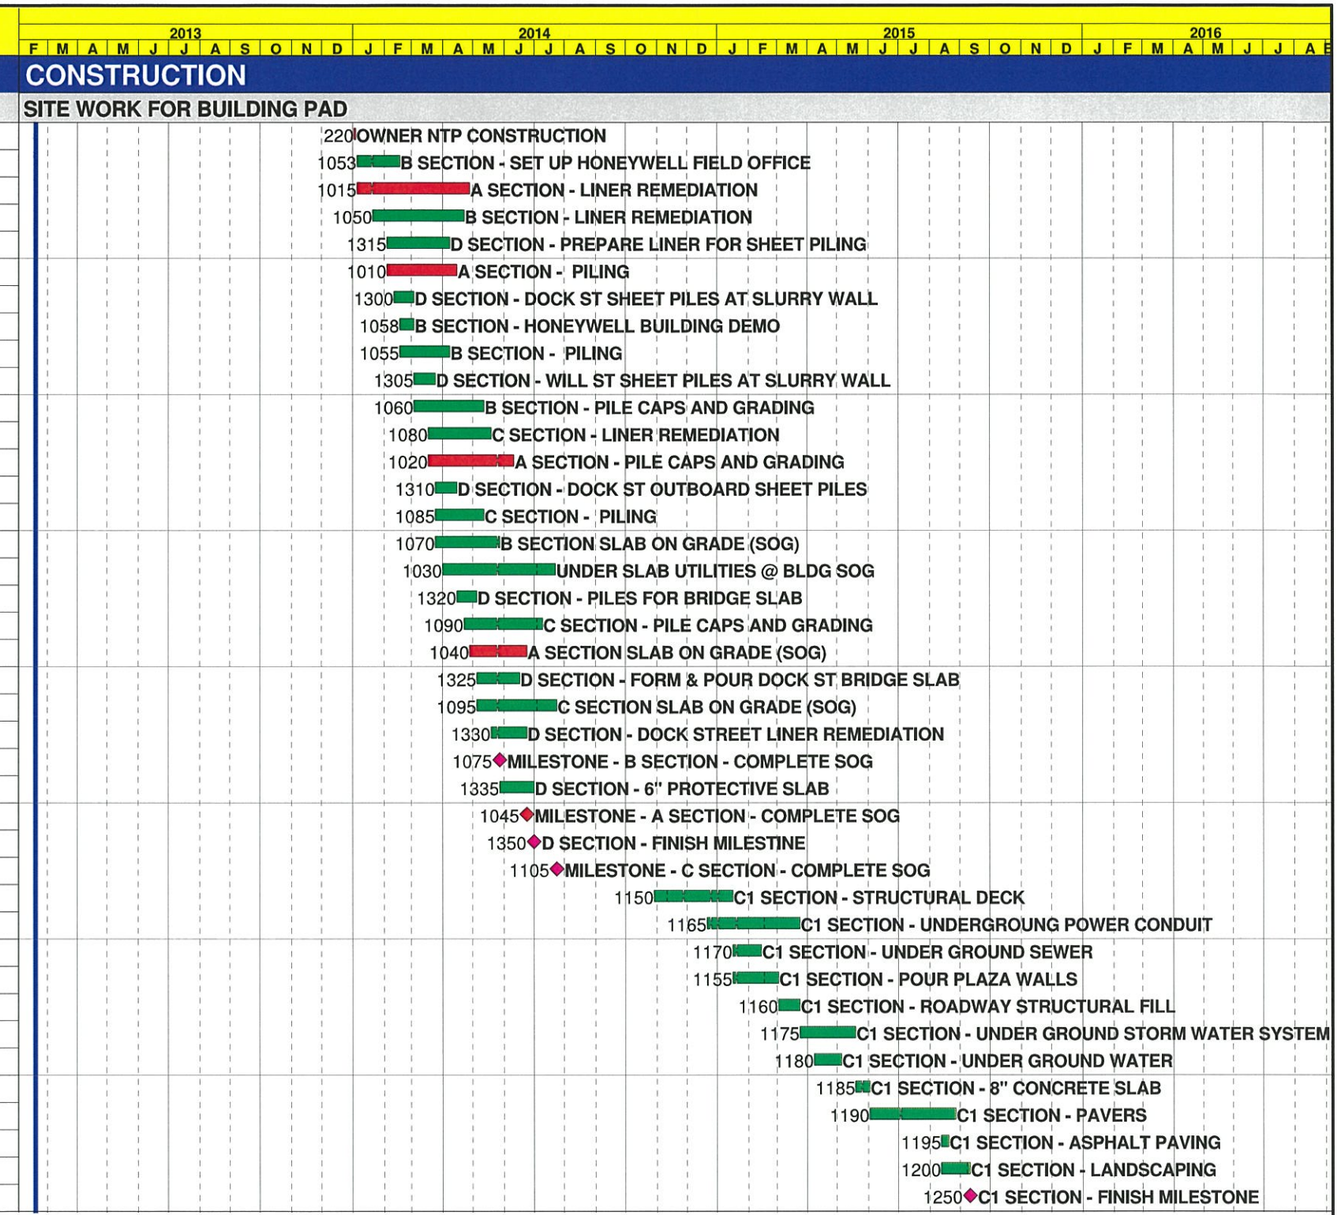

Start Date	18FEB13
Finish Date	02NOV15
Data Date	18FEB13
Run Date	12NOV13 14:57

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

EP15

Sheet 1 of 1

ARMADA HOFFER Construction Co.

Exelon Program & Area Schedule

SITE WORK X EARLY START

HARDT CONSTRUCTION SERVICES, INC. 888-628-6595

Date	Revision	Checked	Approved

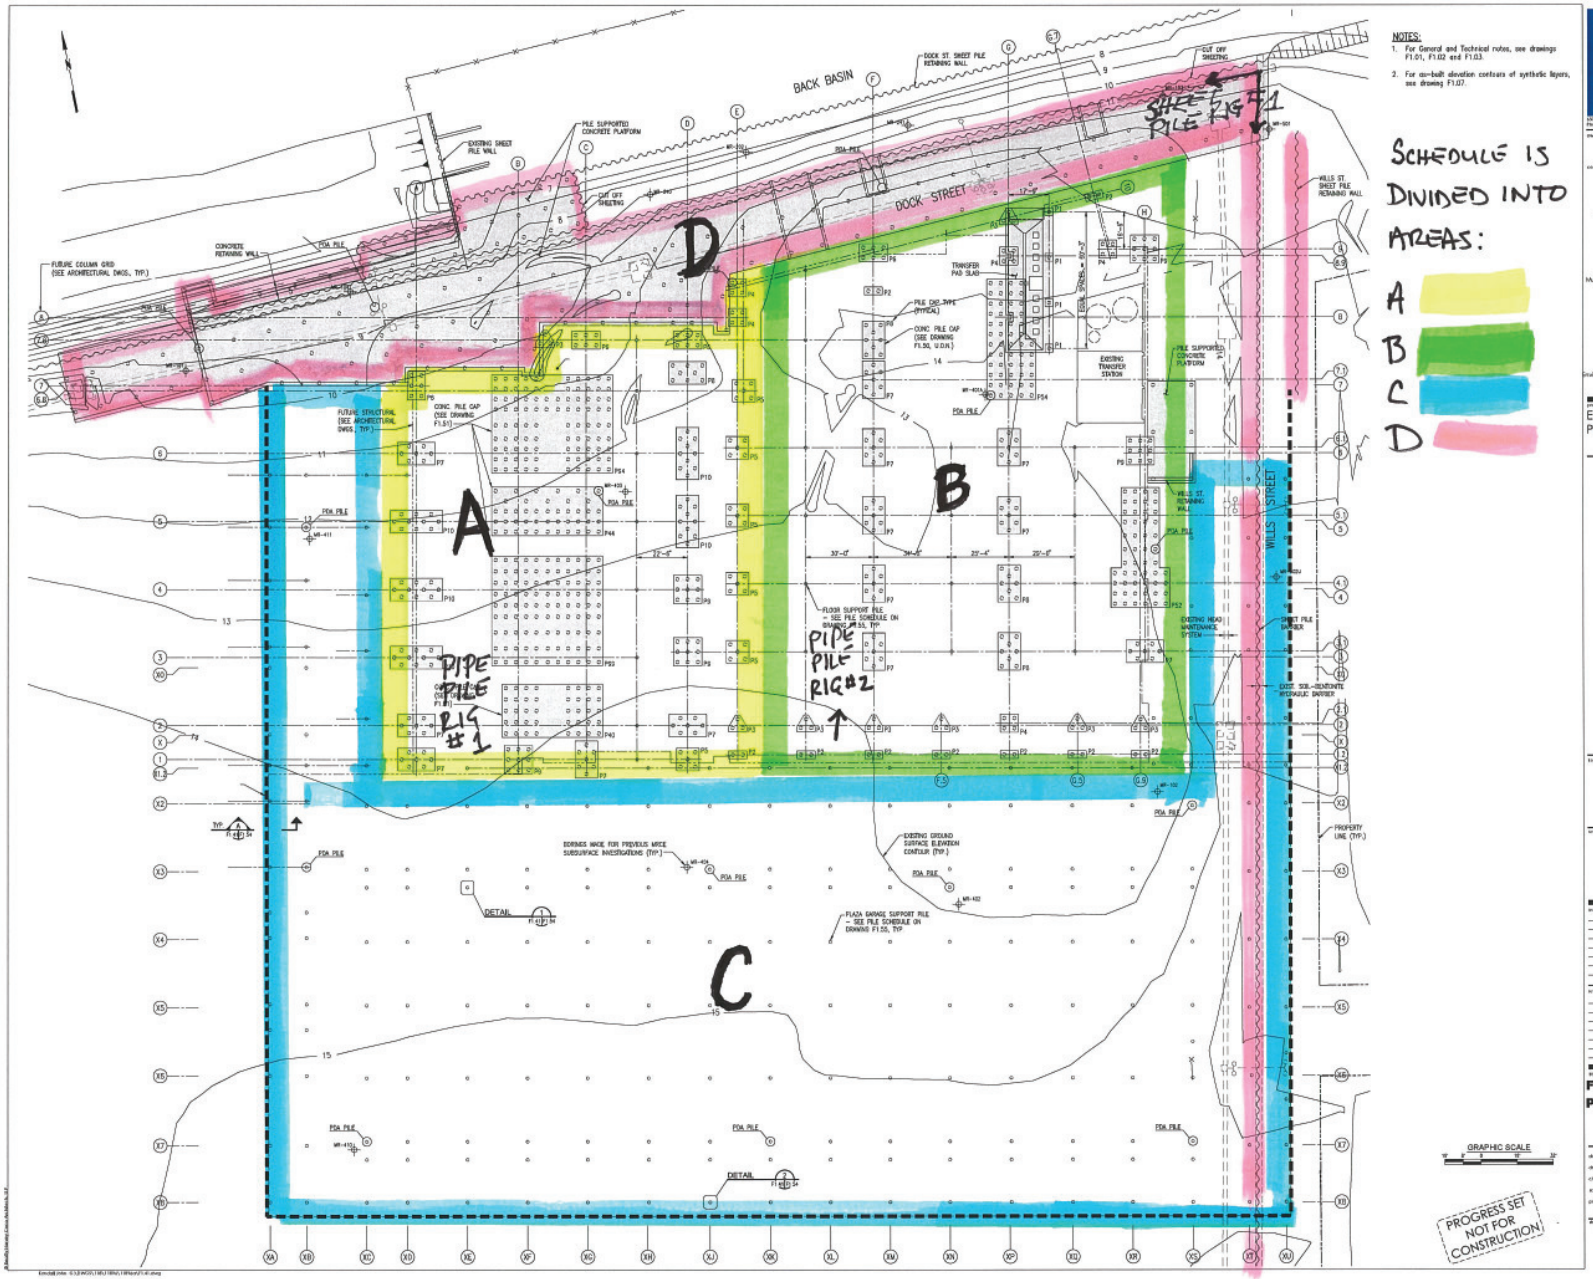

BHC ARCHITECTS

developer: Beatty Development Group

design consultant: Elkus Manfredi Architects

structural engineer: Tadjer Cohen Edelson & Associates

mep & fp engineer: Vandenberg

foundation engineers: Mueser Rutledge Consulting Engineers

civil engineer: Rummel, Klepper & Kahl

landscape architect: Mahan Rykiel Associates

environmental engineer: Environmental Resources Management

project: EXELON BLDG & PLAZA GARAGE

8/1/13

title: FOUNDATION PARTIAL PLAN

F1.41
